


ROOTE ORIGIN SYSTEM / STARTING WITH UBE

MVP scope & costing proposal

Ube Farm Cooperative | Davao, Philippines
From Root to Story visual foundation

Revised: 3 October 2026
Valid until 2 November 2026

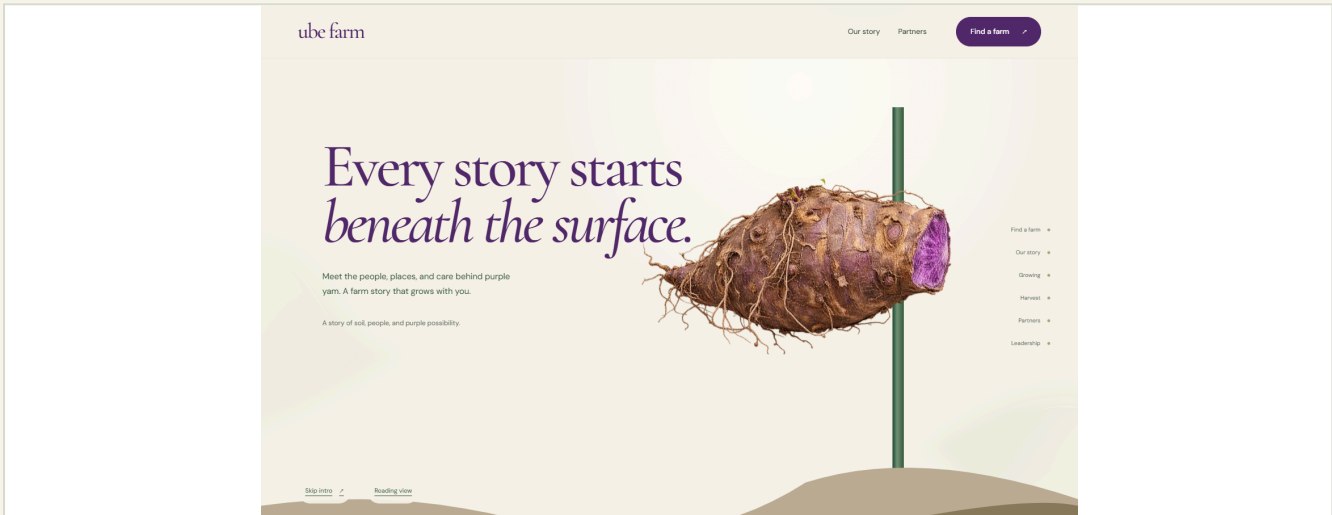

Existing prototype retained as the visual foundation. Inventory and backend interfaces are part of this expanded MVP.

A memorable farm discovery website supported by a protected system that follows each produce batch from farming and harvest to its processor and intended brand owner or distributor. Ube is the first crop.

PROPOSED COMBINED PROJECT FEE	TARGET DELIVERY
₱220,000 Negotiable One-time development	10 weeks Weekly milestones, pilot acceptance and operator handover.

This revised quotation includes building a new Roote Origin backend and reusing the existing From Root to Story prototype. It replaces the earlier PHP 60,000 landing-page-only quotation; PHP 220,000 is the combined project total, not an additional charge on top of it. Prior payments or separately agreed prototype fees will be reconciled in the final agreement.

New backend included

Confirmed scope: build the Roote Origin backend as part of this MVP. The new system includes protected accounts, database records, batch workflows and approved public QR summaries.

01 / INCLUDED DELIVERABLES

What the MVP includes

Help visitors discover the cooperative's farms and produce, give authorized ecosystem members access to connected batch records, and let consumers scan a public summary for the specific batch behind a partner product.

01	Animated landing page	Retain the root drop, green trellis, growing vine, tip-leaf lookup, descending stories, partner leaves and root leadership board. Include mobile layouts, skip-intro and reduced-motion reading.
02	Farm & produce inventory	Search and filter approved farms and their produce under Roote Origin. Show public profiles, crop/variety, harvest or availability information and published batch links. Start with ube; the data model allows other produce.
03	Ecosystem accounts & roles	Invite/login, password recovery and a member dashboard for administrators, growers, processors, brand owners and distributors. Authorized members can read the full permitted batch history; editing is limited by role and assignment.
04	Farming & harvest records	Unique batch ID; farm, plot/site, grower, produce/variety, planting date, agreed farming activities and input notes; harvest date, quantity and unit. Include validation, status and a dated edit history.
05	Processor & recipient links	Record who processed the batch, when and where, link the source harvest batch to its processed lot, and identify the intended brand owner or distributor. Preserve the origin chain for authorized members.
06	Public per-batch QR	Preview and publish an approved consumer summary on a stable batch URL. Download QR artwork in PNG/SVG for partner cafes, restaurants or packaging. Scanning or entering a batch ID opens that specific summary.
07	Admin editing & pilot setup	Manage farms, produce, partners, users, batches, public visibility and manually recorded availability. Assisted setup for up to 10 farms, 20 batches and 25 accounts; normal self-service records can be added afterward.
08	Quality, launch & handover	Responsive and role-access testing; HTTPS deployment; basic public-page SEO; database backup setup and one restore check; source, documentation, one training session and 30-day in-scope defect support.


MERN stack: MongoDB database, Express API on Node.js 26 and React frontend; TypeScript across frontend/backend. Verify the runtime and hosted MongoDB, authentication and storage plans at kickoff. One cooperative ecosystem, English and one production deployment.

Easy content and color changes

Interface text and colors stay in a centralized constants file. Operational farm, produce and batch data is edited through the protected dashboard and stored in the database.

One batch, a connected story

Roote Origin links the farming record to harvest, processing and the brand owner or distributor. A consumer sees only the approved public summary.



PARTICIPANT	CAN VIEW	CAN MANAGE
Administrator	All records in this ecosystem.	Users, farms, produce, batch corrections and publication approval.
Grower / farm team	Authorized batch histories and linked partners.	Assigned farm, growing and harvest records.
Processor	Authorized origin and harvest details.	Assigned processing events, lot links and recipients.
Brand owner / distributor	Full permitted history of assigned batches.	Assigned receipt/allocation acknowledgement and own partner details.
Consumer / public visitor	Published farm pages and approved batch summaries.	No backend editing; no login needed to scan.

Protected ecosystem data

Member view: agreed farming details, harvest and processing data, linked recipients and record history. Server-side permission checks restrict access by role and batch assignment; the cooperative approves the visibility rules in Week 1.

Approved public QR summary

Consumer view: batch ID, produce, farm/location, approved growing summary, harvest date, processor and brand/distributor names where approved. Personal contacts, internal notes and commercial information remain private unless explicitly approved for publication.

Two kinds of discovery

Farm lookup and farm QR open a farm profile. Batch lookup and batch QR open a batch summary. Administrators can unpublish a summary without deleting its private history. A stable URL keeps printed QR artwork usable after approved content updates; physical printing is excluded.

The MVP records information supplied by ecosystem participants. QR traceability does not independently certify authenticity, organic status, export eligibility or regulatory compliance. The initial workflow supports one source harvest batch per processed lot; mixed-origin blending and complex split/merge accounting require separate scope.

Investment for the expanded MVP

DEVELOPMENT ALLOCATION	AMOUNT
Public landing page & inventory Prototype refinement, public farm/produce catalogue, profiles and responsive reading view.	₱60,000
Backend foundation & member access Database/API, authentication, roles, server-side access checks and member navigation.	₱45,000
Batch records & traceability workflow Farming, harvest, quantities/status, processor/recipient links, admin forms and edit history.	₱55,000
Consumer summaries & batch QR Publication approval, public batch pages, ID/QR lookup and downloadable artwork.	₱25,000
QA, security checks & pilot review Permissions, public/private separation, mobile/camera tests and two revision rounds.	₱20,000
Deployment, training & handover HTTPS launch, backups/restore check, documentation, training and launch defect support.	₱15,000

Total project fee – negotiable **₱220,000**

PHP 220,000 is a scope-based estimate for a focused custom full-stack MVP serving a Davao cooperative. It includes the existing visual direction plus operational records, permissions and public batch pages. Provider packages differ; this is a negotiable project estimate, not a statistical Davao market average.

Proposed payment milestones

Kickoff 40% Written scope approval; before Week 1 work begins.	₱88,000
Core records review 30% Week 5: accepted farm, growing and harvest workflows on staging.	₱66,000
MVP acceptance 20% Week 9: accepted end-to-end flow and consolidated revisions.	₱44,000
Launch & handover 10% Week 10: before production launch and source transfer.	₱22,000

One combined quotation

This PHP 220,000 proposal includes the public website and the new Roote Origin backend. It supersedes the prior landing-only estimate. Operating costs and optional maintenance are listed separately on page 6.

O4 / WEEKLY DELIVERY PLAN

Ten weeks from kickoff to launch

Target: 10 working weeks after written scope approval, complete kickoff inputs and initial payment. Weeks are sequential delivery targets, not fixed calendar dates. Client review, missing data or approved scope changes may extend the schedule.

WEEK	MILESTONE	PLANNED OUTPUT
Week 1	Confirm the system	Approve fields, roles, public/private rules, pilot data, one design direction and the batch workflow.
Week 2	Build the foundation	Set up MongoDB, the Express/Node.js API, authentication, environments and server-side access rules.
Week 3	Organize the ecosystem	Build farm, produce, partner and account management; prepare the public inventory structure.
Week 4	Capture farming details	Implement planting, plot/site, care/input notes and authorized record editing.
Week 5	Track harvest batches	Implement batch IDs, harvest dates, quantities, availability/status and record history.
Week 6	Connect processing & recipients	Link processors, processed lots, brand owners and distributors to their source batches.
Week 7	Publish the consumer view	Build approved batch summaries, publication controls, stable URLs and QR downloads.
Week 8	Connect the landing experience	Integrate live public inventory, lookup and batch links; refine mobile and scroll behavior.
Week 9	Review & accept the pilot	Run workflow, role, QR and device checks; complete two consolidated in-scope revision rounds.
Week 10	Launch & transfer	Configure HTTPS/backups, check restore, train operators, hand over source and start defect support.

Review cadence

Review working features on staging at each milestone. Consolidated client feedback is requested within two working days. Week 9 includes the agreed pilot review and two revision rounds; approved changes may shift Week 10.

05 / OPERATING BUDGET & BOUNDARIES

Keep the pilot focused

Development, running costs and future enhancements are agreed separately.

Operating costs, paid separately

Operating allowance: PHP 2,500–5,000/month for a small Node.js/Express API, MongoDB hosting, authentication/file storage, backups and essential service usage; domain PHP 1,000–3,500/year. These are planning allowances, not provider quotations. Client-owned accounts pay actual charges; traffic, storage, email usage, exchange rates and plan changes affect cost.

First-year base budget: ₱251,000–₱283,500

Project fee + 12 months of operating allowance + domain. Excludes optional maintenance, premium domains, paid asset licenses, excess provider usage and applicable taxes. Any applicable tax treatment will be stated in the final quotation/invoice.

Optional ongoing maintenance

Optional maintenance: PHP 4,000/month for up to four hours of routine checks, minor fixes/updates and support. New features and extra hours are separately quoted. This service is not automatically billed and is separate from the included 30-day defect support.

Meaning of inventory in this MVP

Inventory means a farm/produce catalogue with recorded batch quantities and manually maintained availability. It does not include a full warehouse ledger, reservations, sales orders, POS, invoicing or real-time stock synchronization.

Outside the initial MVP

E-commerce, payments, POS, accounting, shipment tracking and full warehouse/ERP stock control.

Existing-system integrations, bulk legacy migration, IoT/sensor feeds and offline/native apps.

Independent multi-tenant organizations, extra languages, major new 3D scenes and media production.

Mixed-origin batch blending, complex split/merge reconciliation and automated stock reservations.

Blockchain, independent certification, export compliance verification and advanced analytics.

Plan provider costs at kickoff

Confirm the database, API, file-storage and email plans in Week 1. Use client-owned accounts, an agreed backup retention policy and a modest pilot workload. Additional usage and paid service upgrades are charged by the providers.

06 / ACCEPTANCE & AGREEMENT

Ready to pilot, clear to approve

Acceptance before launch

- 01 An authorized grower, processor and recipient can complete the agreed batch journey; linked records persist after refresh and re-login.
- 02 Public inventory shows only approved farms/produce and batch links. Farm IDs/links and batch IDs/QRs resolve to their respective pages.
- 03 Logged-out and unauthorized API requests cannot read private or unassigned records; role-restricted edits and publication controls are enforced.
- 04 A production QR opens the correct published summary without login; unpublished/unknown IDs and denied camera access have clear recovery states.
- 05 Mobile, keyboard and reduced-motion views work; Android/Chrome and iPhone/Safari QR checks, backup restore and operator handover are completed.

Client inputs & pilot support

Provide the approved cooperative identity/photos, Sir Marco's official roles, pilot farm/produce/batch records, processor and brand/distributor details, role assignments and public-field consent. Confirm the workflow and data visibility, supply client-owned service accounts, and return consolidated feedback within two working days of each review.

Assisted onboarding covers up to 10 farms, 20 batches and 25 accounts. These are setup allowances, not software record limits. Creating ordinary records through delivered forms is included; bulk migration, developer-assisted entry beyond the allowance or new record types are separately negotiated.

Two consolidated revision rounds refine the agreed MVP. A new design concept or changed workflow is a scope change. The 30-day defect-support period starts at launch and covers defects in delivered features; ongoing data entry, new features, provider outages and 24/7 incident response are excluded.

Costing is negotiable

The proposed project fee, payment terms and delivery arrangements are negotiable. Final costing will be mutually agreed in writing based on the approved scope and schedule.

Additional features incur additional cost

Additional features, integrations, major design changes or expanded workflows will incur additional cost depending on complexity and negotiations. A separate quotation and any timeline adjustment will be agreed in writing before that work begins.

For client discussion. Final scope, total fee, operating arrangements, schedule and payment terms must be mutually confirmed in writing before work begins.
