
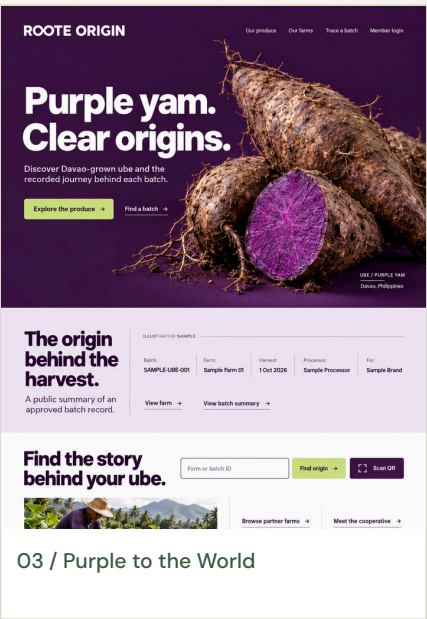


DAVAO, PHILIPPINES / STARTING WITH UBE

Project-based MVP scope & costing

Ube Farm Cooperative | Davao, Philippines
Based on the latest three-design client presentation

Prepared: 5 October 2026
Valid until: 4 November 2026

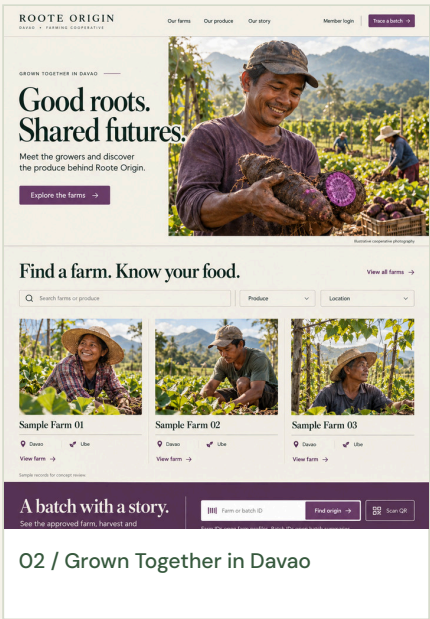

Three proposed directions. Choose one for implementation; imagery and records shown are illustrative.

One selected public website design, a protected ecosystem portal and a MongoDB-backed batch history, delivered as one defined project. Consumers discover farms and scan approved batch summaries; members manage the permitted origin records.

PROPOSED PROJECT FEE	TARGET DELIVERY
₱220,000	10 weeks
Negotiable / one-time development	Milestones, pilot review and handover

Prepared for the project-based option in the latest client presentation. The PHP 220,000 fee covers the combined website and new backend, not three separate design builds. Any previous payments or prototype charges will be reconciled before the final agreement to avoid duplicate billing.

Confirm before commitment

This is a proposed engagement, not an accepted contract. Confirm one design, its motion sequence and asset reuse, weekly development availability, and the single-source processing workflow before agreeing the final fee and start date.

01 / DELIVERABLES

One design, one connected MVP

Help visitors discover the cooperative's farms and produce, give authorized ecosystem members access to connected batch records, and let consumers scan a public summary for the specific batch behind a partner product.

01	One public design	Implement one approved direction from the three concepts. Include its agreed scroll story, responsive mobile composition, accessible navigation and reduced-motion view. Reuse the current prototype and artwork where suitable.
02	Farm & produce catalogue	Search farms and produce; filter the catalogue by crop/location; open approved farm profiles, availability and published batch links. Begin with ube; ordinary produce records can be added later.
03	Protected member portal	Login, password recovery and assigned member dashboards. Administrators, growers, processors and brand owners/distributors see permitted batch history; backend rules restrict edits and record access.
04	Growing & harvest history	Farm, plot/site, grower, produce/variety, planting date and agreed care/input notes. Add harvest ID, date, quantity/unit and status, with validation and dated correction history.
05	Processing & recipients	Record the processor, date/place, processed lot and intended brand owner or distributor. Link one source harvest batch to each processed lot and preserve its origin history.
06	Public batch QR	Admin preview, approval, publish/unpublish and a stable public URL per batch. Farm/batch ID lookup, camera scanning and PNG/SVG QR downloads; public consumers need no login.
07	Admin & pilot onboarding	Manage farms, produce, partners, accounts, batch records and publication. Assisted entry of up to 10 farms, 20 batches and 25 accounts; ordinary records remain self-service afterward.
08	Test, launch & handover	Feature and permission testing, two review rounds, HTTPS production deployment, public-page SEO basics, backups and one restore check. Source/documentation, one training session and 30-day defect support.

MERN: MongoDB, Express API, React and Node.js 26; TypeScript across frontend and backend. One cooperative ecosystem, English, one staging environment and one production deployment. Agree hosting, storage, email and backup retention at kickoff.

Editable copy, colors and operational data

Interface text and colors stay in a centralized constants file. Operational farm, produce and batch data is edited through the protected dashboard and stored in the database.

From the farm to the public QR

A connected member record and a separately approved consumer summary for each batch.

01 / RECORD Farm & growing Origin, planting and care	02 / RECORD Harvest batch Date, quantity and ID	03 / RECORD Processor Processing and lot link	04 / RECORD Brand / distributor Intended recipient
--	---	---	--

PARTICIPANT	CAN VIEW	CAN MANAGE
Administrator	All records in this ecosystem.	Users, farms, produce, batch corrections and publication approval.
Grower / farm team	Authorized batch histories and linked partners.	Assigned farm, growing and harvest records.
Processor	Authorized origin and harvest details.	Assigned processing events, lot links and recipients.
Brand owner / distributor	Full permitted history of assigned batches.	Assigned receipt/allocation acknowledgement and own partner details.
Consumer / public visitor	Published farm pages and approved batch summaries.	No backend editing; no login needed to scan.

Private member records

Member view: agreed farming details, harvest and processing data, linked recipients and record history. Server-side permission checks restrict access by role and batch assignment; the cooperative approves the visibility rules in Week 1.

Approved public summary

Consumer view: batch ID, produce, farm/location, approved growing summary, harvest date, processor and brand/distributor names where approved. Personal contacts, internal notes and commercial information remain private unless explicitly approved for publication.

Farm QR and batch QR serve different purposes

Farm lookup and farm QR open a farm profile. Batch lookup and batch QR open a batch summary. Administrators can unpublish a summary without deleting its private history. A stable URL keeps printed QR artwork usable after approved content updates; physical printing is excluded. Partners display the appropriate batch QR and replace it when the batch changes.

The MVP records information supplied by ecosystem participants. QR traceability does not independently certify authenticity, organic status, export eligibility or regulatory compliance. The initial workflow supports one source harvest batch per processed lot; mixed-origin blending and complex split/merge accounting require separate scope.

03 / FEE AND PAYMENT MILESTONES

Proposed project investment

DEVELOPMENT ALLOCATION	AMOUNT
Selected public design & catalogue One design, agreed motion, responsive layouts, public farm/produce pages and prototype reuse.	₱60,000
Backend foundation & member portal MongoDB/API, login and recovery, role/assignment rules and member navigation.	₱45,000
Batch history & operational forms Growing/harvest records, quantities/status, processor/recipient links and correction history.	₱55,000
Publication, lookup & batch QR Approved summaries, visibility controls, ID/camera lookup and QR artwork downloads.	₱25,000
QA, access checks & pilot reviews Public/private tests, workflow persistence, mobile/camera checks and two review rounds.	₱20,000
Launch, training & handover HTTPS, backups/restore check, pilot assistance, documentation and delivered-defect support.	₱15,000

Total project fee / negotiable **₱220,000**

A scope-based custom MVP estimate for a Davao cooperative: animated public experience plus operational records, permissions and QR publication. It is not a basic brochure-site package or a measured Davao market average. The existing PHP 220,000 combined estimate is retained, subject to confirmation of the selected redesign and workflow.

Payments follow deliverable milestones

Kickoff / 40% Before Week 1: written scope, chosen design and workflow approved; kickoff inputs ready.	₱88,000
Core records / 30% Target Week 5: client accepts farm, growing and harvest workflows on staging.	₱66,000
MVP acceptance / 20% Target Week 9: client accepts the end-to-end flow and two consolidated review rounds.	₱44,000
Launch readiness / 10% Target Week 10: approved release, restore check and handover package ready; payable before production launch/source transfer.	₱22,000

Fixed scope, subject to written agreement

The final negotiated project fee covers the approved deliverables. Milestone weeks are targets; payment is tied to the listed delivery or acceptance event. No extra work is billed without an approved change request. Hosting and optional maintenance are separate.

O4 / DELIVERY IN WEEKS

Ten weeks from kickoff to launch

Target: 10 delivery weeks after written scope approval, complete kickoff inputs and the kickoff payment. Confirm working availability before commitment. Client feedback, missing content, service-account delays and approved changes may move the schedule.

WEEK	MILESTONE	PLANNED OUTPUT
Week 1	Confirm the system	Confirm one design, pilot records, roles, public fields and whether processors combine harvests.
Week 2	Build the foundation	Build MongoDB, the Express/Node.js API and sign-in. Test account access and role restrictions.
Week 3	Organize the ecosystem	Build farm, produce, partner and account forms. Test saving, editing and permitted access.
Week 4	Capture farming details	Add planting, plot and care records. Test required fields, dates and record corrections.
Week 5	Track harvest batches	Add harvest IDs, quantities and status. Review the growing-to-harvest workflow with pilot users.
Week 6	Connect processing & recipients	Link processors, lots and recipients. Test origin links and each participant's permitted access.
Week 7	Publish the consumer view	Build public summaries, approvals and QR downloads. Test published, private and unknown IDs.
Week 8	Connect the landing experience	Connect the catalogue and chosen design. Check mobile, QR and reduced motion. First review round.
Week 9	Review & accept the pilot	Complete the second review round, pilot acceptance and final workflow, permission and device checks.
Week 10	Launch & transfer	Launch with HTTPS and backups. Check restore, train operators and confirm the support handover.

Review and testing cadence

Testing begins with feature development in Week 2. Review working milestones on staging; consolidated design/flow review rounds are in Weeks 8 and 9. Feedback is requested within two working days. Schedule changes will be communicated and agreed, rather than hidden in the week targets.

05 / DESIGN CHOICE AND SCOPE BOUNDARIES

Choose the experience. Keep the pilot clear.

The three designs share the same catalogue, member portal and batch QR features. The fee funds one selected design.

01 From Root to Story

Forest-green vine journey, leaf-mounted origin lookup, farm previews and people behind the roots.

02 Grown Together in Davao

Grower photography, an early searchable farm catalogue and a separate farm/batch lookup.

03 Purple to the World

Bold ube imagery, product-to-origin storytelling and prominent public batch information.

Approve the selected motion before development

The deck describes proposed motion. Confirm the final opening, scroll sequence, mobile behavior and asset reuse against the current prototype. Existing photographic 2.5D artwork may be reused; a new fully modeled 3D scene or major additional asset production requires separate scope.

What inventory means here

Inventory means a farm/produce catalogue with recorded batch quantities and manually maintained availability. It does not include a full warehouse ledger, reservations, sales orders, POS, invoicing or real-time stock synchronization.

Outside this project fee

E-commerce, payments, POS, accounting, shipment tracking and full warehouse/ERP stock control.

Existing-system integrations, bulk legacy migration, IoT/sensor feeds and offline/native apps.

Independent multi-tenant organizations, extra languages, major new 3D scenes and media production.

Mixed-origin batch blending, complex split/merge reconciliation and automated stock reservations.

Blockchain, independent certification, export compliance verification and advanced analytics.

Single-source batch workflow

The quoted pilot assumes one source harvest batch per processed lot. If processors combine harvests or farms, revise the data workflow, cost and delivery plan before commitment. Physical QR printing, professional photography and paid asset licenses are excluded.

06 / PILOT ACCEPTANCE AND OPERATING COSTS

Ready to run and ready to hand over

Acceptance checks

- 01 Assigned grower, processor and recipient complete the agreed farming-to-recipient flow; linked records persist after refresh and re-login.
- 02 Logged-out and unauthorized API requests cannot read private/unassigned records or perform restricted edits; only administrators publish.
- 03 Only approved farm/produce pages and public batch links appear. ID lookup and production QR open the correct farm or batch; unpublished/unknown records have recovery states.
- 04 The selected design works on mobile, keyboard and reduced motion. Android/Chrome and iPhone/Safari camera checks are completed with agreed test devices.
- 05 HTTPS launch, backup restore check, operator training, source files and editing/deployment documentation are completed.

Client inputs and assisted onboarding

Supply approved identity/photos and leadership roles, pilot farm/produce/batch data, processor/recipient details, account assignments and public-field approval. Confirm whether harvests are combined, provide client-owned deployment accounts, and assign one decision-maker for consolidated feedback.

Assisted onboarding covers up to 10 farms, 20 batches and 25 accounts. These are setup allowances, not software record limits. Creating ordinary records through delivered forms is included; bulk migration, developer-assisted entry beyond the allowance or new record types are separately negotiated.

Operating costs paid separately

Operating allowance: PHP 2,500–5,000/month for a small Node.js/Express API, MongoDB hosting, authentication/file storage, backups and essential service usage; domain PHP 1,000–3,500/year. These are planning allowances, not provider quotations. Client-owned accounts pay actual charges; traffic, storage, email usage, exchange rates and plan changes affect cost.

First-year base allowance: ₱251,000–₱283,500

Project fee + 12 months of operating allowance + domain. Excludes optional maintenance, premium domains, paid asset licenses, excess provider usage and applicable taxes. Any applicable tax treatment will be stated in the final quotation/invoice.

Calculation: ₱220,000 + (₱2,500–₱5,000) x 12 months + ₱1,000–₱3,500 domain/year.

Optional maintenance

Optional maintenance: PHP 4,000/month for up to four hours of routine checks, minor fixes/updates and support. New features and extra hours are separately quoted. This service is not automatically billed and is separate from the included 30-day defect support.

07 / PROPOSED PROJECT-BASED TERMS

Clear delivery and handover

These arrangements apply only if project-based delivery is selected and the final agreement is approved.

Engagement and review

Delivery covers the defined MVP through acceptance, launch, handover and 30-day defect support. Weekly progress updates and scheduled milestone reviews are included. Ongoing operations, daily staff duties, open-ended development and employment availability are outside this project fee.

Two consolidated revision rounds refine the approved design and workflow. Report reproducible acceptance issues against the agreed criteria; in-scope defects are corrected before acceptance. Late feedback moves dependent milestones and does not by itself constitute acceptance.

Source, accounts and data

After full payment, deliver the agreed custom source code and documentation to client-controlled accounts; record ownership/licensing terms in the final agreement. Third-party tools, fonts and assets remain subject to their licenses. The cooperative owns its operational data and is responsible for its accuracy and approved publication.

Included launch support

30 days from production launch for defects in delivered functionality. No automatic maintenance subscription. Daily data entry, new features, third-party incidents and 24/7 response are excluded; a separate support arrangement can be agreed after the pilot.

Costing is negotiable

The PHP 220,000 proposed project fee, milestone percentages and payment terms are negotiable. Final costing, scope, selected design, working availability and launch schedule will be mutually confirmed in writing before development starts.

Additional features incur additional cost

Additional features, integrations, new animation scenes, major redesigns or expanded workflows will incur additional cost depending on complexity and negotiations. Approve a written change request with its deliverables, additional fee and timeline impact before that work begins.

Confirm before kickoff

Selected design and workflow: _____

Final fee, payments and kickoff date: _____

Working availability and client reviewer: _____

For discussion if the client chooses project-based delivery. Selection of a design or receipt of this proposal does not confirm an engagement. Any applicable tax treatment will be stated in the final quotation/invoice.
